


Activity ID	Activity Description	Orig Dur	Early Start	Early Finish
1	SED Review & Approval	164	16FEB09	01OCT09
11	Bidding	23	05OCT09	04NOV09
21	Award Contracts	1	09NOV09	09NOV09
41	Pool Construction	145	30NOV09	18JUN10
61	Reconstruct shop area	79	30NOV09	18MAR10
91	Reconstruct the Library	80	30NOV09	19MAR10
121	Guidance (shell Only)	30	30NOV09	08JAN10
111	Install Elevator	80	04JAN10	23APR10
71	Science room recon. complete 1rm then 2and 3rd	110	31MAR10	31AUG10
31	Abatement 1931 building	3	01APR10	05APR10
51	Abatement of boiler rooms	3	01APR10	05APR10
101	Gym construction	43	03MAY10	30JUN10
151	New Roof	88	03MAY10	01SEP10
81	New Boilers & UV's	88	17MAY10	15SEP10
220	Punch List Pool	10	18JUN10	01JUL10
131	Reconstruct guidance	41	25JUN10	20AUG10
171	Nurse/ Principal office	41	25JUN10	20AUG10
141	MEP work on roof	40	28JUN10	20AUG10
230	Abatement all areas	25	30JUN10	03AUG10
161	Slate roof repairs	59	01JUL10	21SEP10
200	Punch List for building all Primes	60	11OCT10	31DEC10
210	Close Out of Primes	60	28MAR11	17JUN11

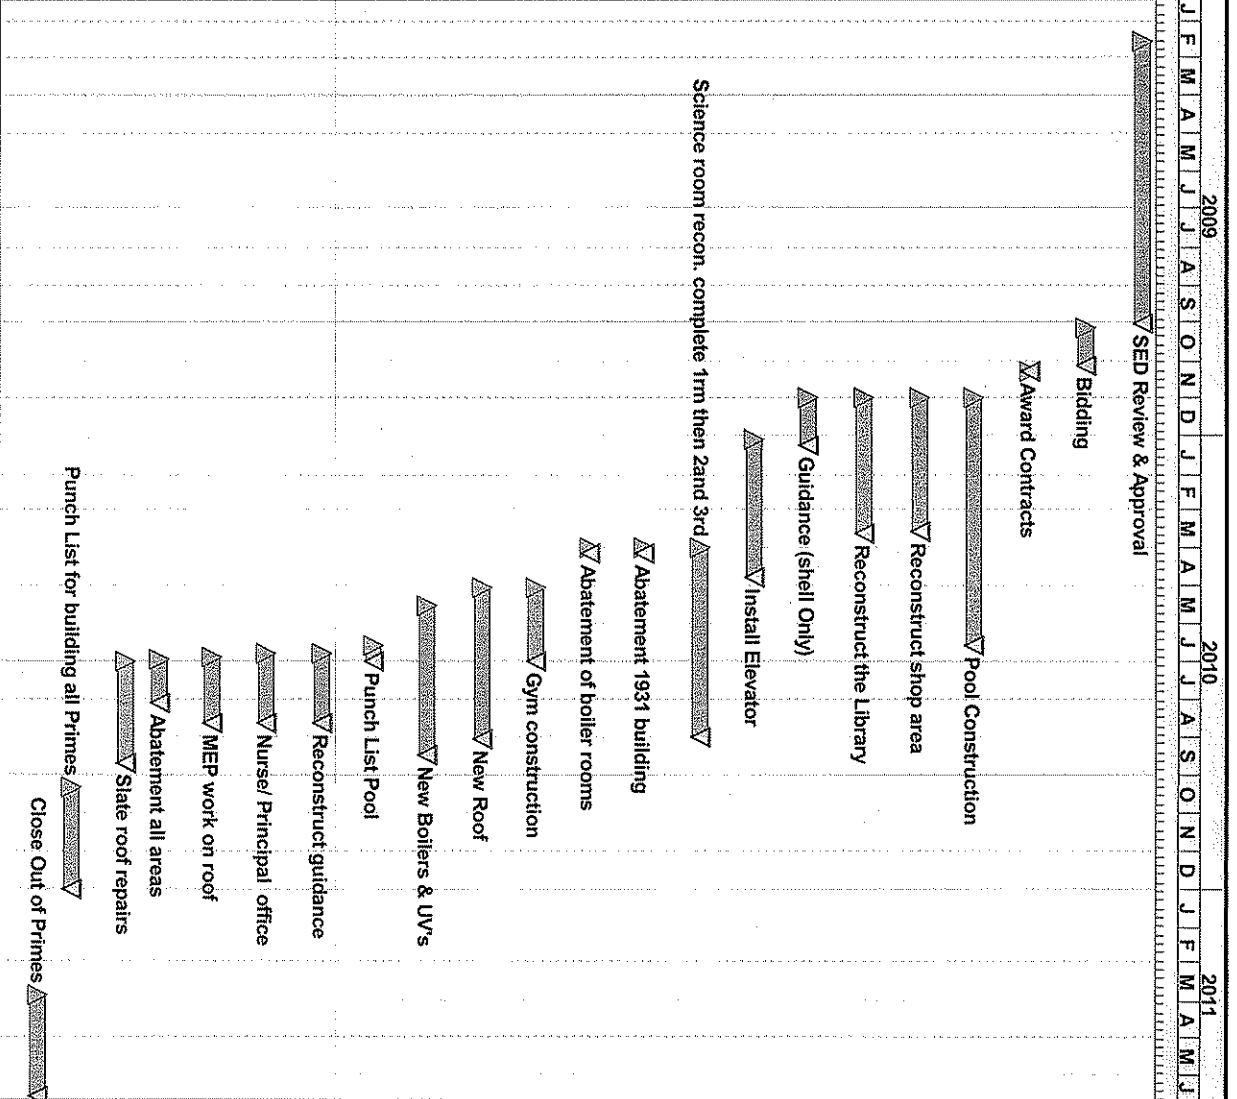

Start Date	12JAN09	PCSC
Finish Date	12JAN09	
Date Date	17SEP09 14:50	
Run Date		

Pocantico Renovations Project  
Pocantico Renovations  
DRAFT PROJECT SCHEDULE

Sheet 1 of 1

Date	Revision	Checked	Approved

© Primavera Systems, Inc.
